Construction/Design Process Update

School Board Meeting - January 26, 2022 North Central High School and Central Campus






















North Central HS / Central Campus

Design Schedule



September 2021 to Jan 2022

North Central High School Construction Documents:

Schmidt Associates completed Construction Documents for Phase 2a & 2b and assisted with evaluating bids

Forecasted Progress for Next 6 Months:

- Start Construction of Phase 2 Field House Addition, Transportation Building Renovation, Transportation Storage Building, Tennis Courts, Bus Storage Lot, Bus Staging Areas, Student Parking Lot
- Finish Construction Documents for Phase 3











Central Campus work to

extend through 2026













North Central HS / Central Campus Site Plan




















Building Plan Design

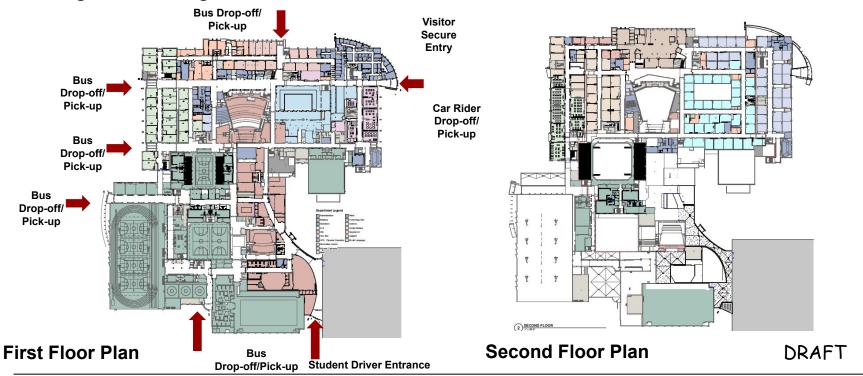



















North Central HS / Central Campus

Process & Engagement Since Sept 2021

- Regulatory Agencies/Utilities Submittals & Reviews
 The following are in Process for Phase 2 Work:
 - Drainage Submittal
 - Special Use 2 (School) Zoning Approval
 - Department of Public Works
 - AES/IPL Overhead Power Line
 - Citizens Water/Sanitary
 - Improvement Location Permit
 - State and City Building Planning Review
- Stakeholders
 - Over 25 Coordination meetings with various departments and school leadership




















Phase 1 - Central Plant - Heating and Air Conditioning Upgrades



- Boiler work complete
- Transformer set
- Currently working on Chiller scope

Phase 1 - Auditorium Renovations (Current through May 2022)



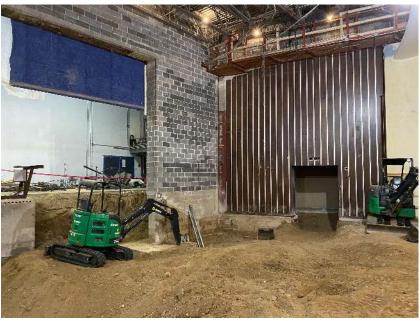

Excavation work to create new Orchestra Pit

Phase 1 - Auditorium Renovations (Current through July 2022)




Phase 2 Graphics - Athletic Entrance - West Side (June 2022 - February 2024)



Phase 2 Graphics - Fieldhouse Entry Corridor (June 2022 - February 2024)



Phase 2 Graphics - Fieldhouse (June 2022 - February 2024)

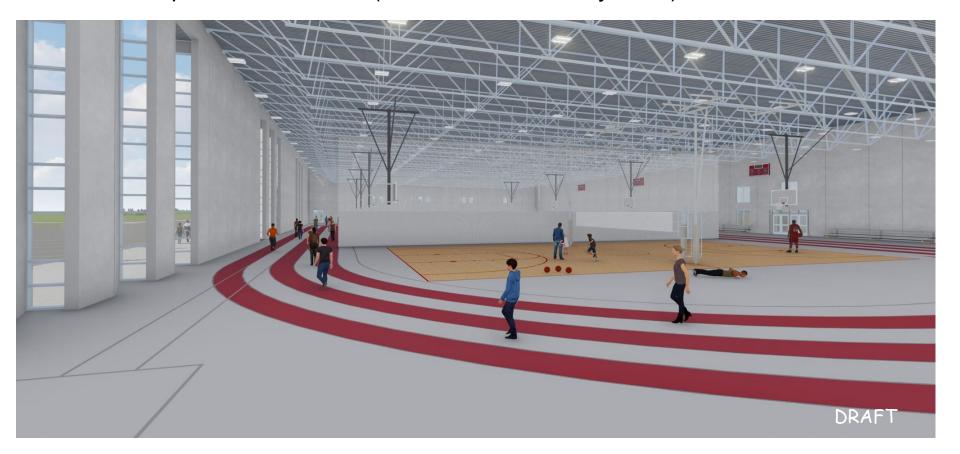

Phase 2 Graphics - Multi-Purpose Rooms within Fieldhouse Addition (June 2022 - February 2024)



Transportation Building

Phase 2 Graphics - Finishes June - July 2022



DRAFT

Phase 3 Graphics - Main Entrance - East Side (Sept 2022 - Dec 2025)



Phase 3 Graphics - Gathering Stair/Barista (Sept 2022 - Dec 2025)



Phase 3 Graphics - Panther Pathways (Sept 2022 - Dec 2025)



Phase 3 Graphics - Library (Sept 2022 - Dec 2025)



Phase 3 Graphics - Staff Think Tanks (Sept 2022 - Dec 2025)



North Central Central Campus


Construction Phasing Graphic


PHASES OF WORK

- 1 Central Plant and Auditorium Under Construction Construction
- 2 West Gym, Centralized Bus Storage, Tennis Courts Bid
- 3 Main Building CD's
- 4 Athletic Fields/Stadium
- 5 JEL
- 6 Operations Service Center

Forecasted Progress for Next 6 Months

- Complete Phase 1 Construction
- Start Construction Phase 2 & Central Bus Storage
- Bid Phase 3

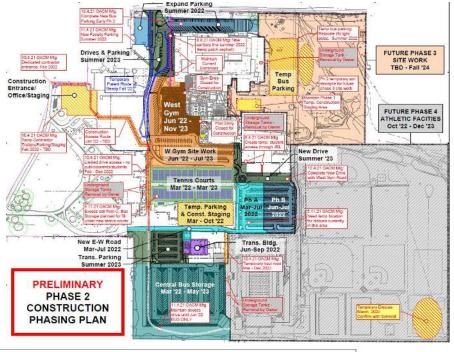



Pre-Referendum Community Commitments North Central High School/Central Campus

Minimize Traffic Impact on surrounding Neighborhoods	/
Minimize Sound Impact	/
Address Drainage Issues on South end of Campus	/
Improve Neighborhood Connectivity	/
Create Neighborhood Resource Hub (i.e. Meeting Rooms, Activity Spaces, Fields)	/
Consolidate Transportation and Operation Services (Maint., Security, Technology)	/



